


Concept of Terminal Expansion




Terminal Exterior


Current – Main Level

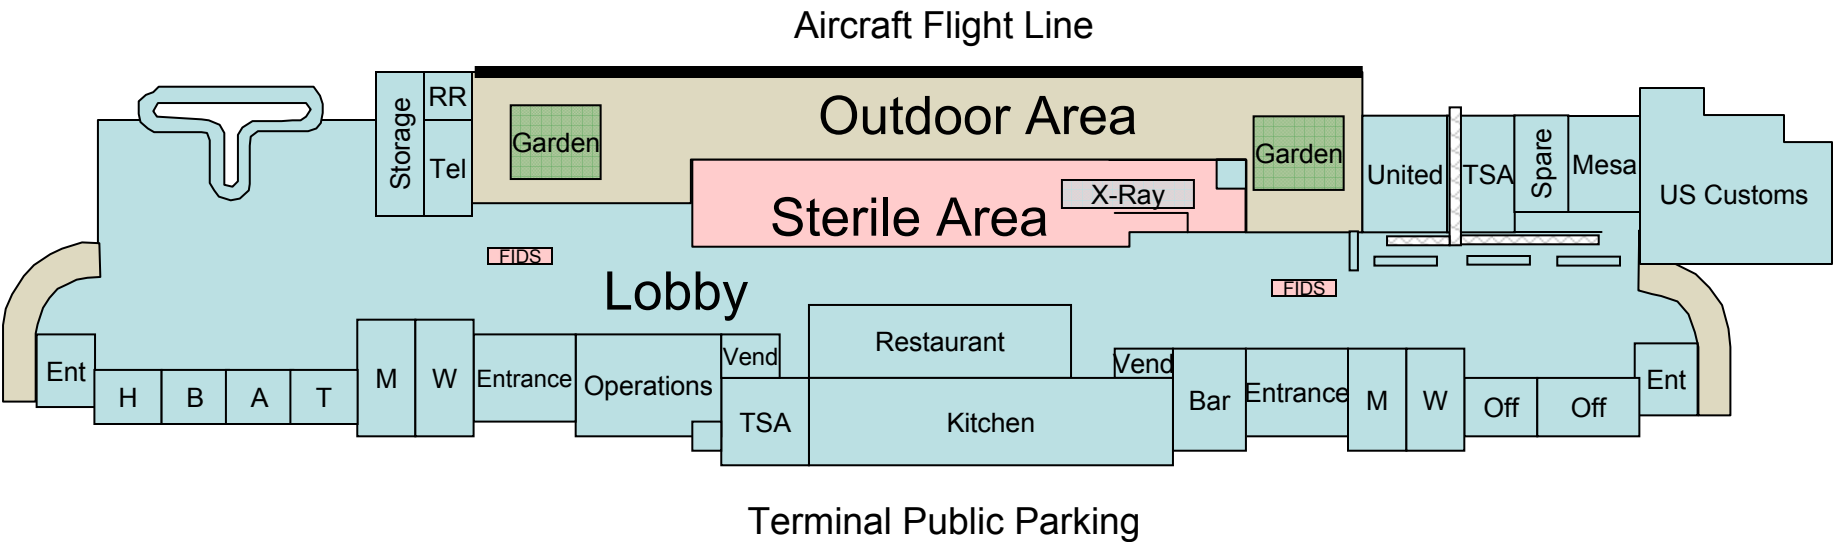


Expanded – Main Level

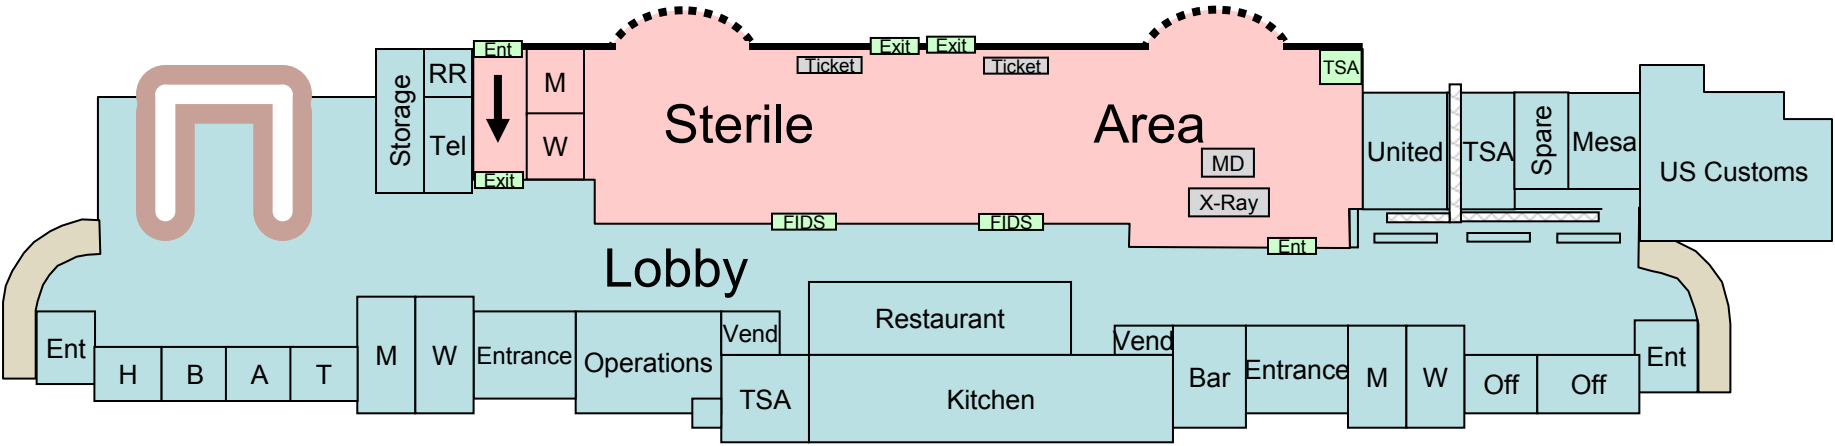

Expanded – Main Level

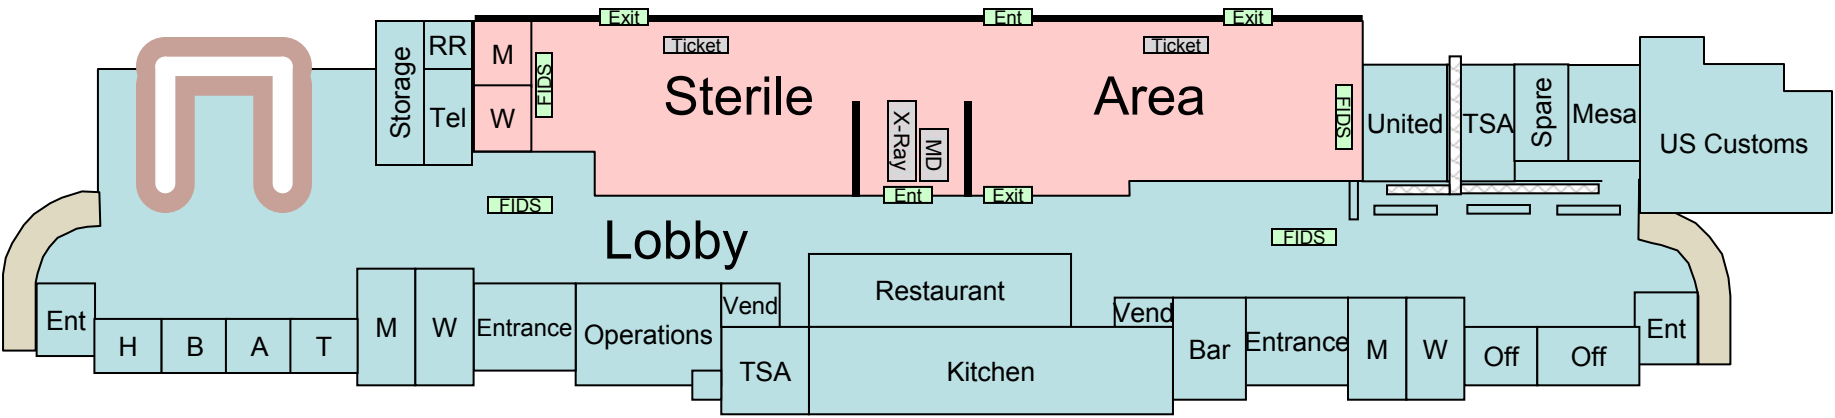


Expanded – Main Level

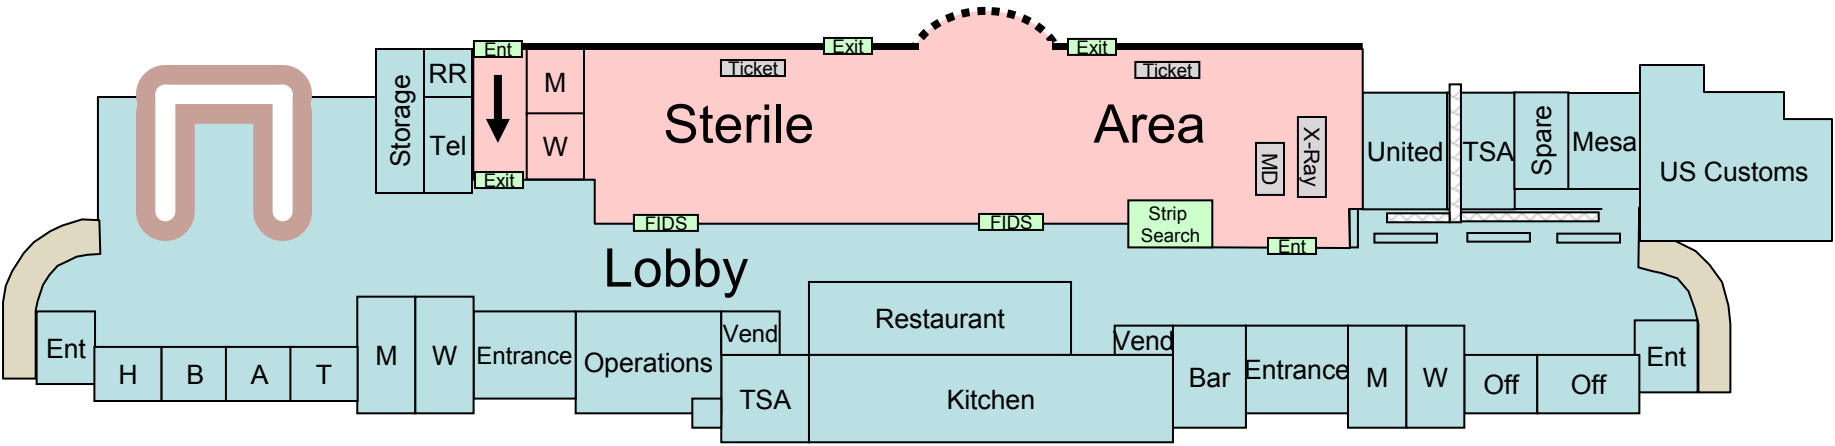


Phasing

Current – Starting point

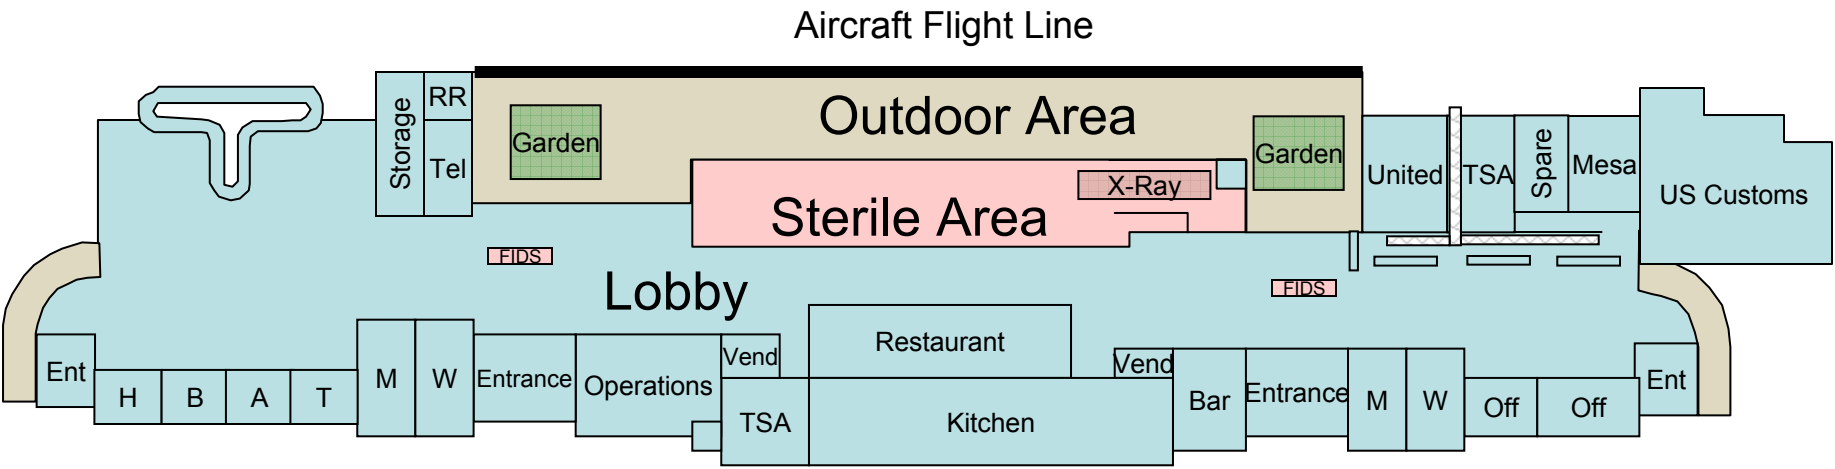


Phase 1 – Build Interior TPWA

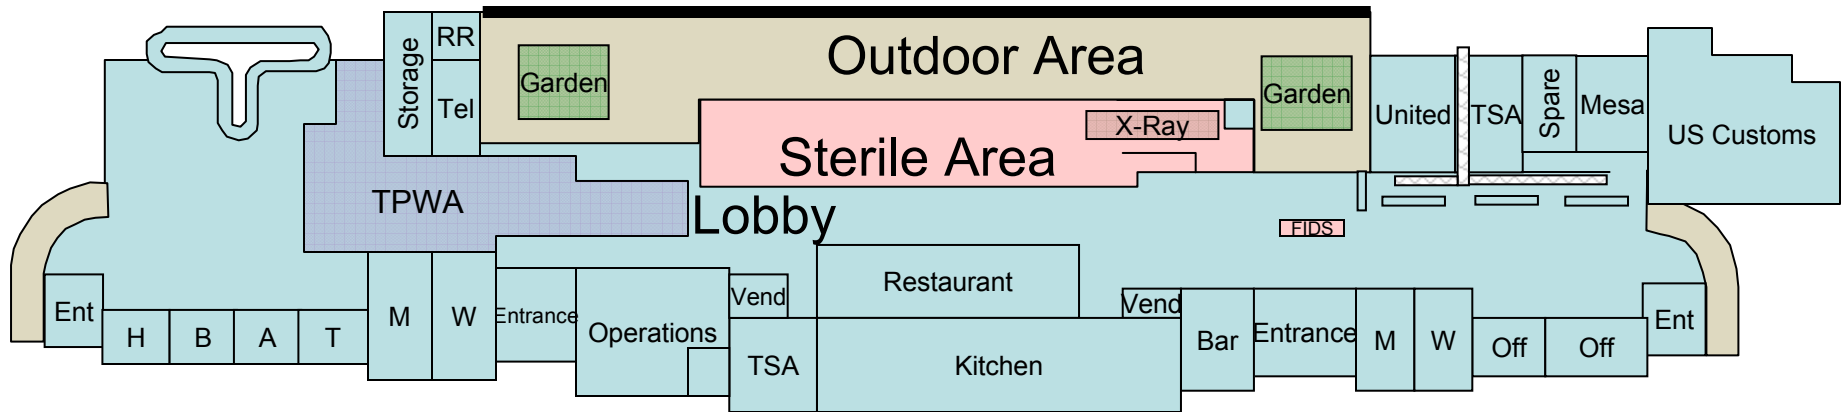


- Remove FIDS, Remove Pay Phones
- TPWA must have durable, painted, solid, attractive walls
 - Must be approved by TSA
- Install necessary power for X-Ray and Metal Detector, Install Phone

Phase 2 – Build Protected Walkways

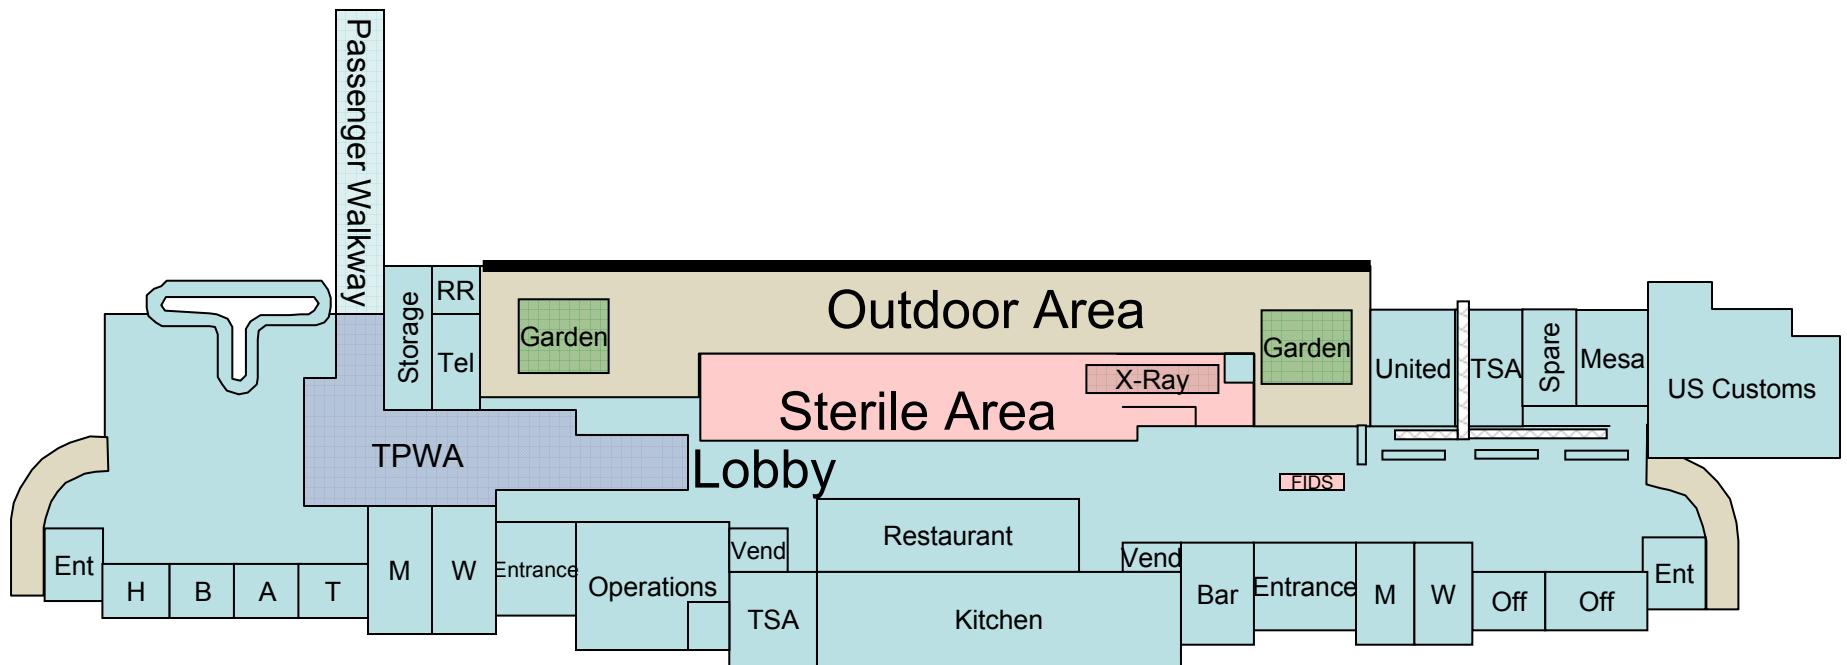


- Walkway must be protected on West Side and Roof
 - Open on east side with railing to prevent unintended egress
- Must be Lighted for nighttime use
- Include Large “Welcome” & “Enter Here” signs at end of walkway
- Install Construction Camera at end of Walkway
- NOTE: Once installed, the TPWA and walkway cannot be disturbed in any way

Phase 3 – Transition to TWPA

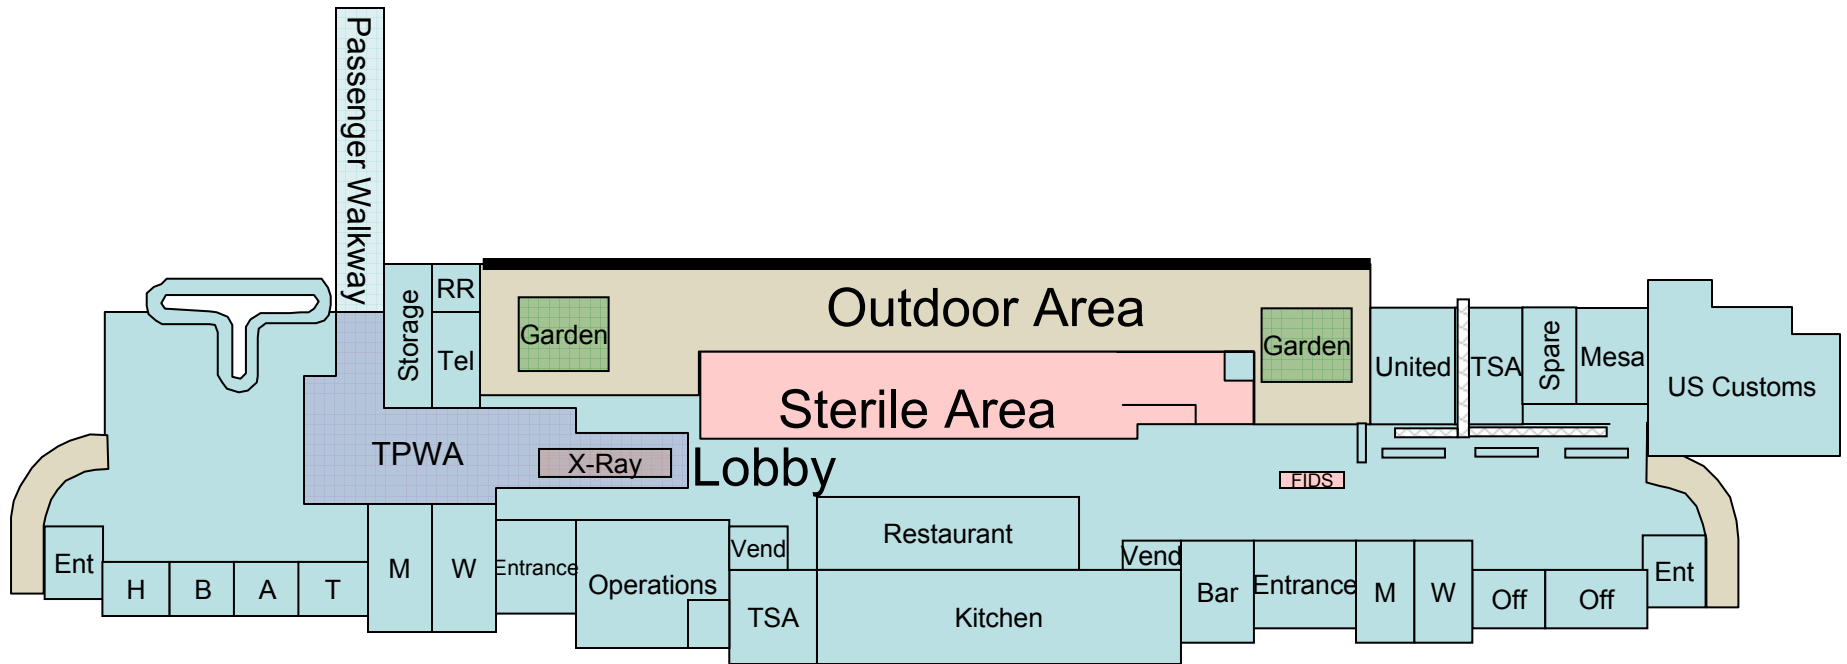


- Coordinate Move with TSA
- Move X-Ray and Metal Detector
- Move Passenger Seating into place

Phase 4 – Install Temp Flightline Electrical

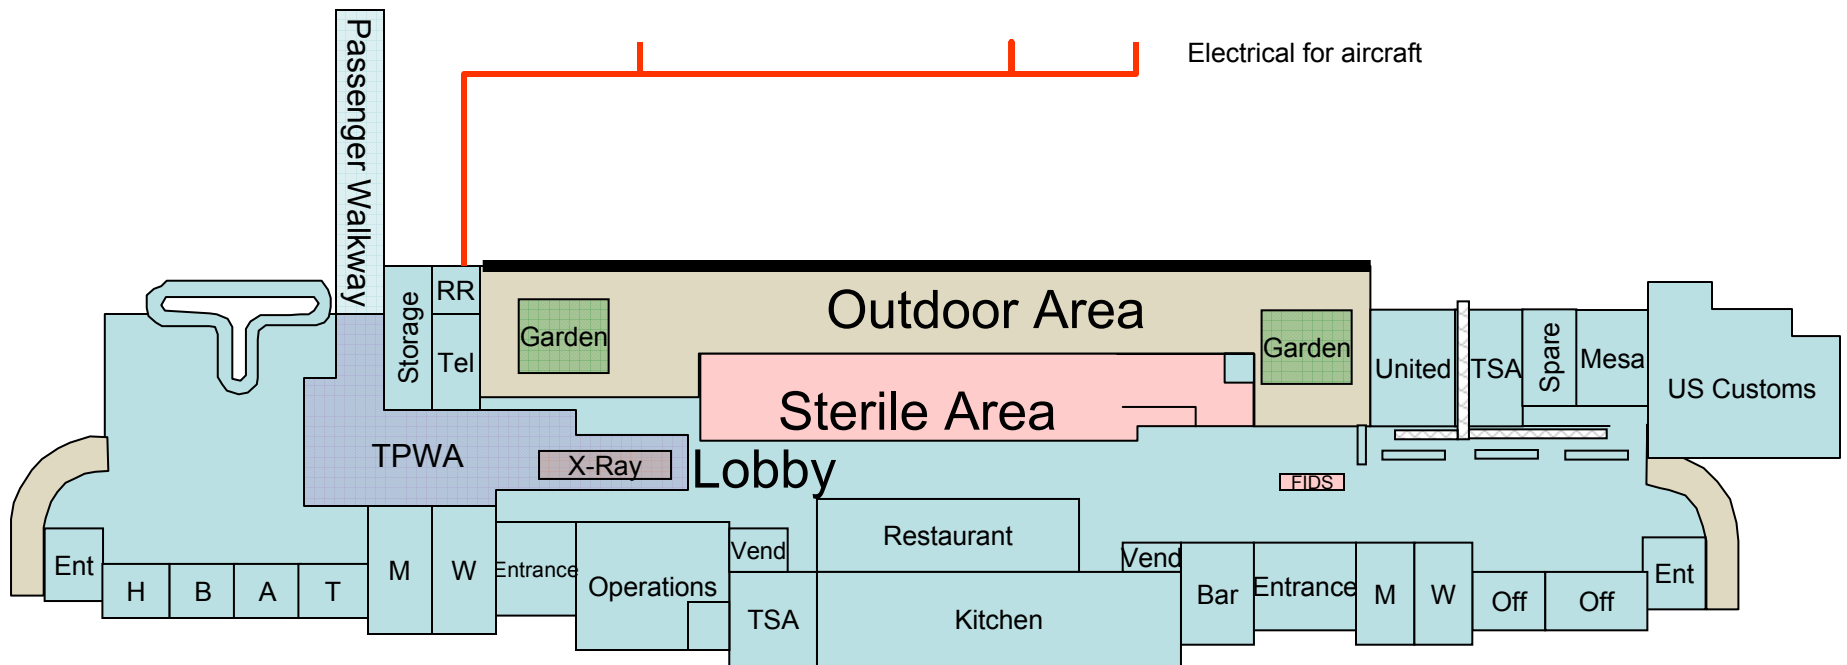


- Meet with Airline Representatives to determine requirements
 - Consider aircraft ground equipment
 - Battery chargers
 - Etc.

Phase 5 – Build Construction Fencing

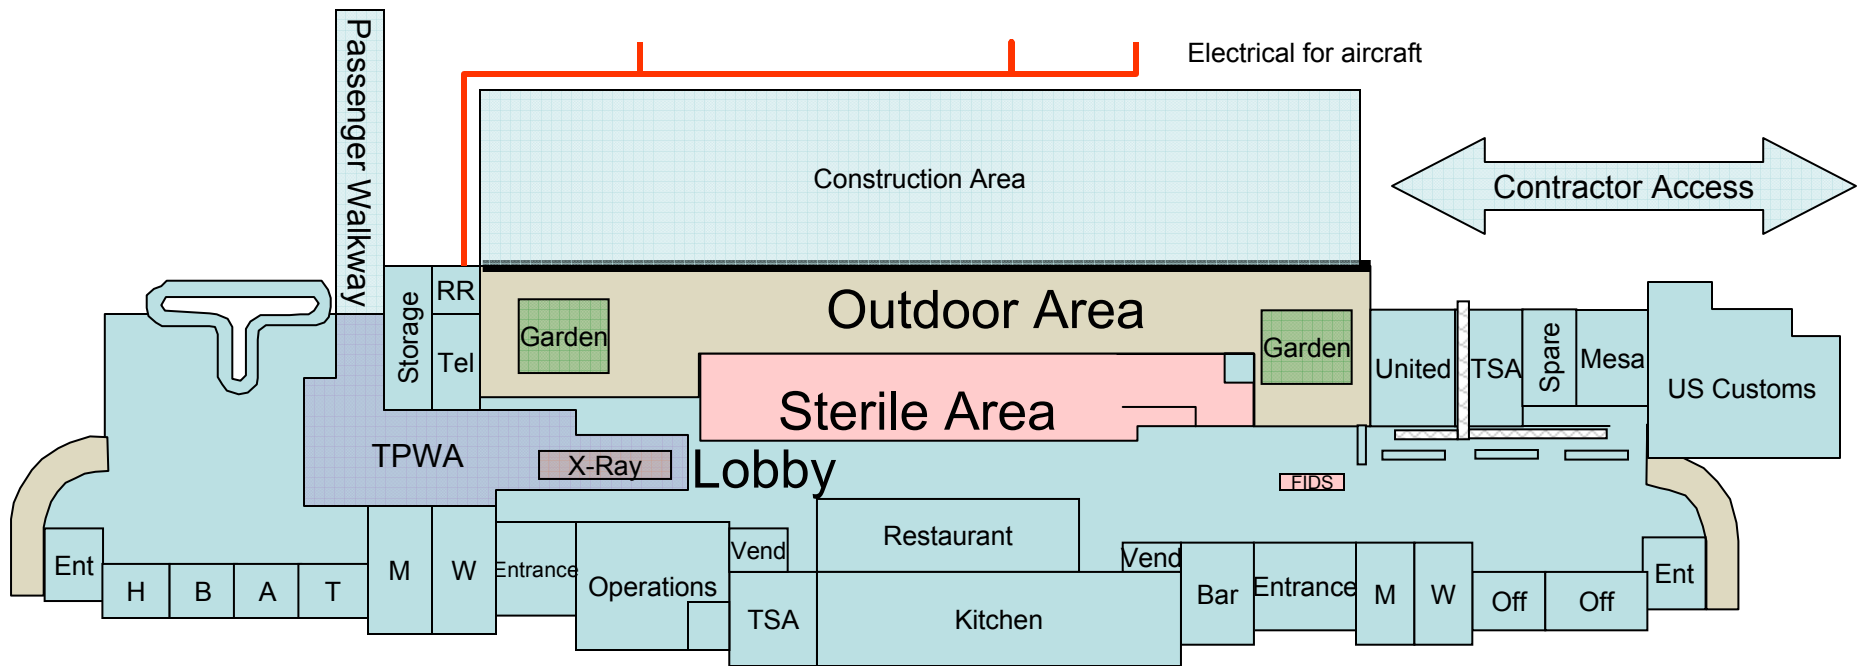


- All Construction Material must be stored within fenced area
- FOD sensitive area must be kept clean at all times
- Install lockable Swing Gate for access on West side of construction area.
- Contractor truck access through Drive through gate near customs.
- Do NOT Block ground crew access to aircraft areas.

Phase 6 – Main Construction

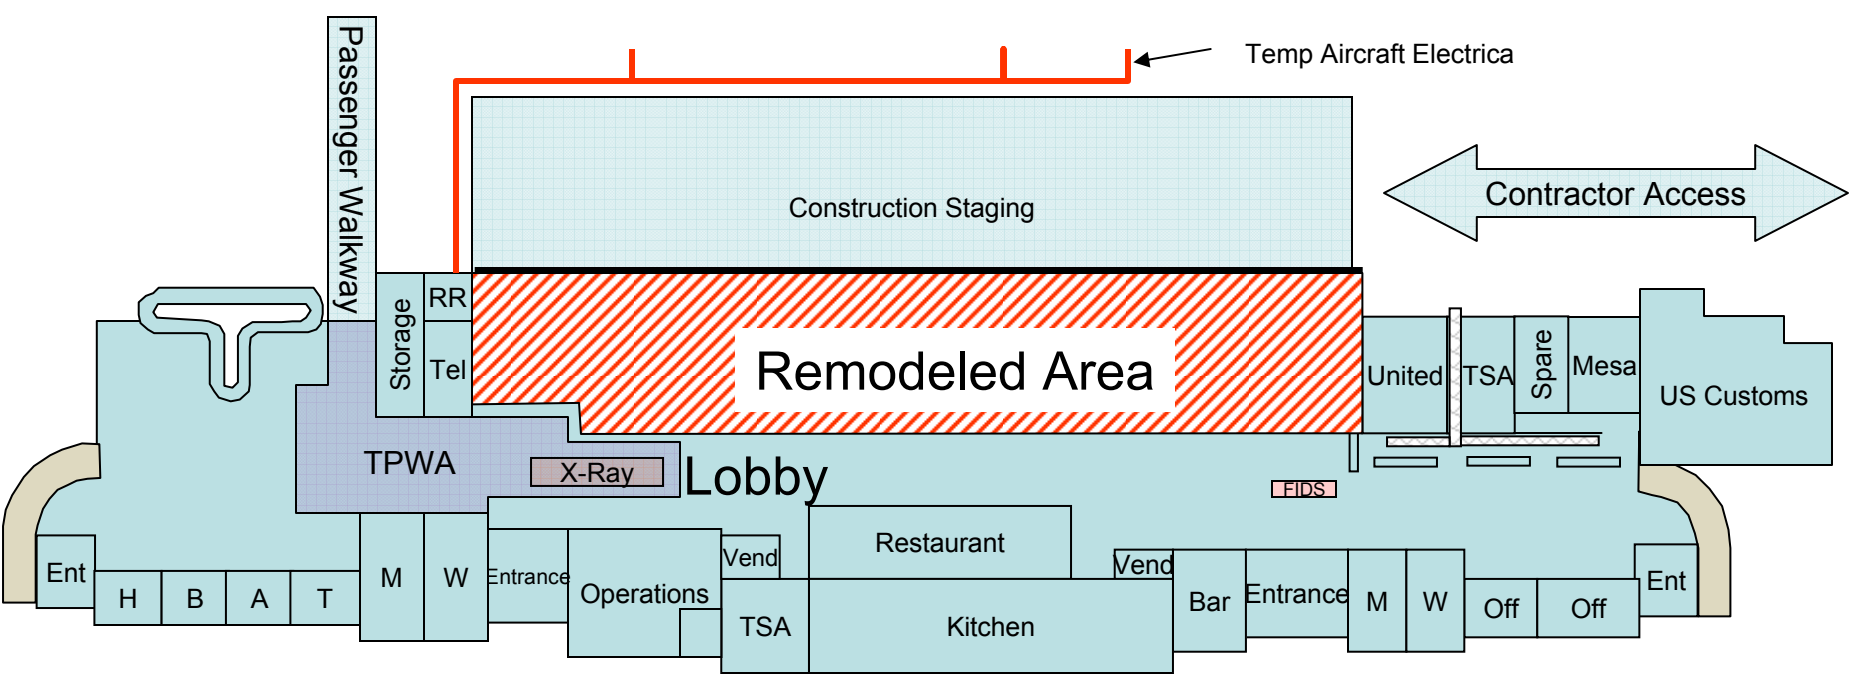


Phase 7 – Complete Main Construction

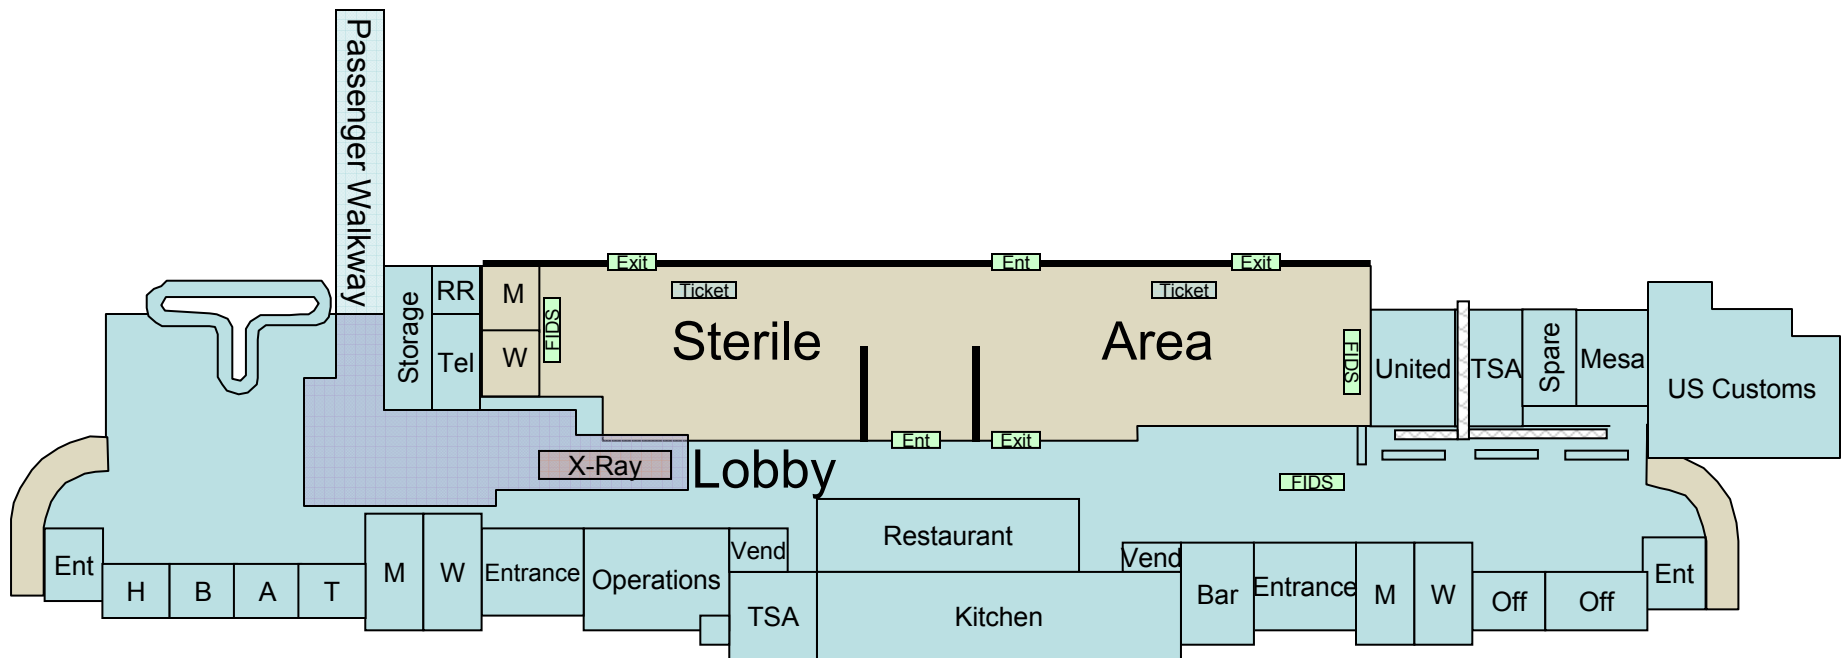


- Remove Construction Fencing
 - Clean up Areas
- Remove Temporary Electrical once area is certified for Aircraft use

Phase 8 – Transition to new Area

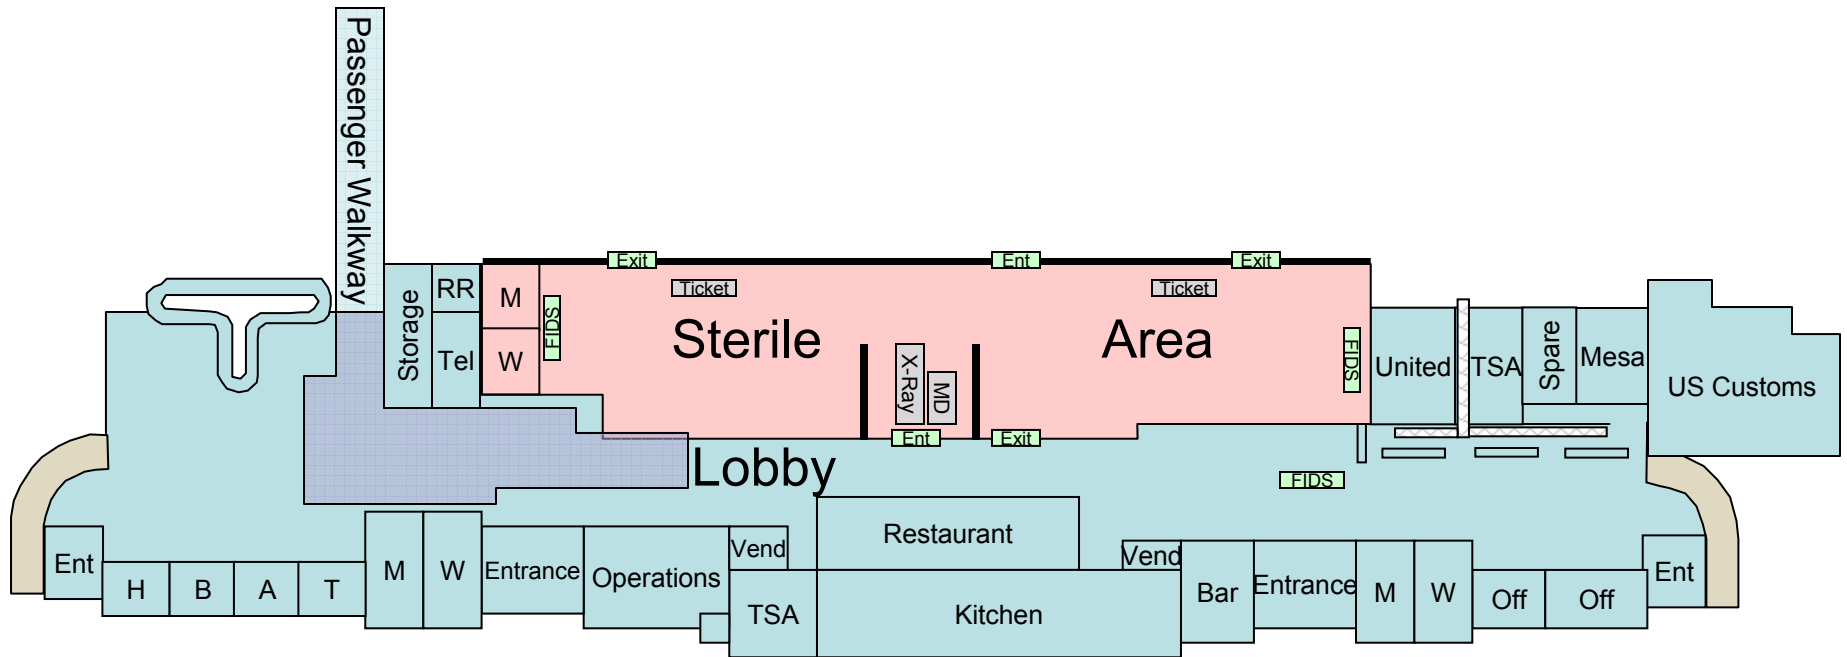


- Coordinate with TSA
- Move X-Ray and Metal Detector back to new Area

Phase 9 – Remove TWPA, Replace FIDS

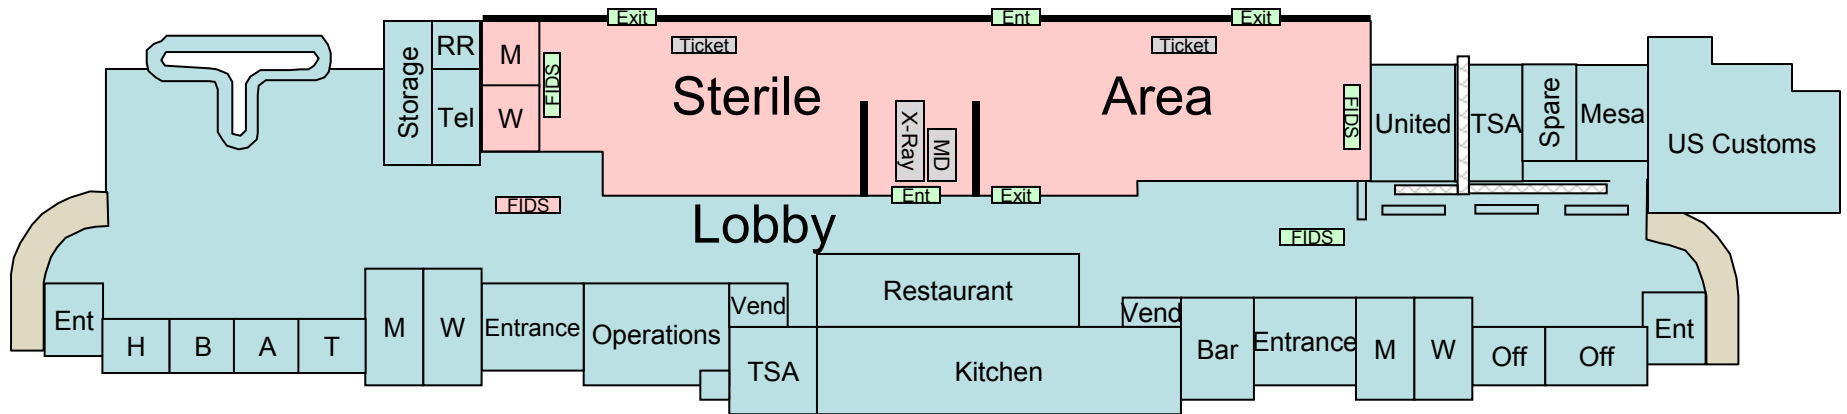


- Remove TWPA and Walkway

Phase 10 – Replace Baggage Belt System

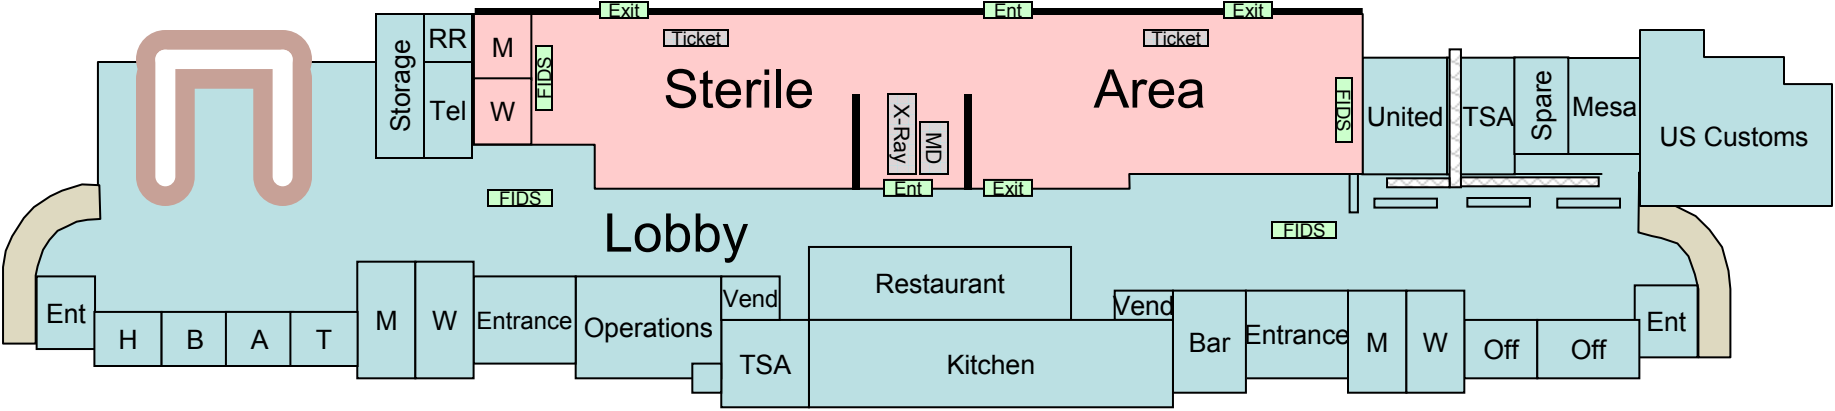

Close Out Phase – Punch List and Close

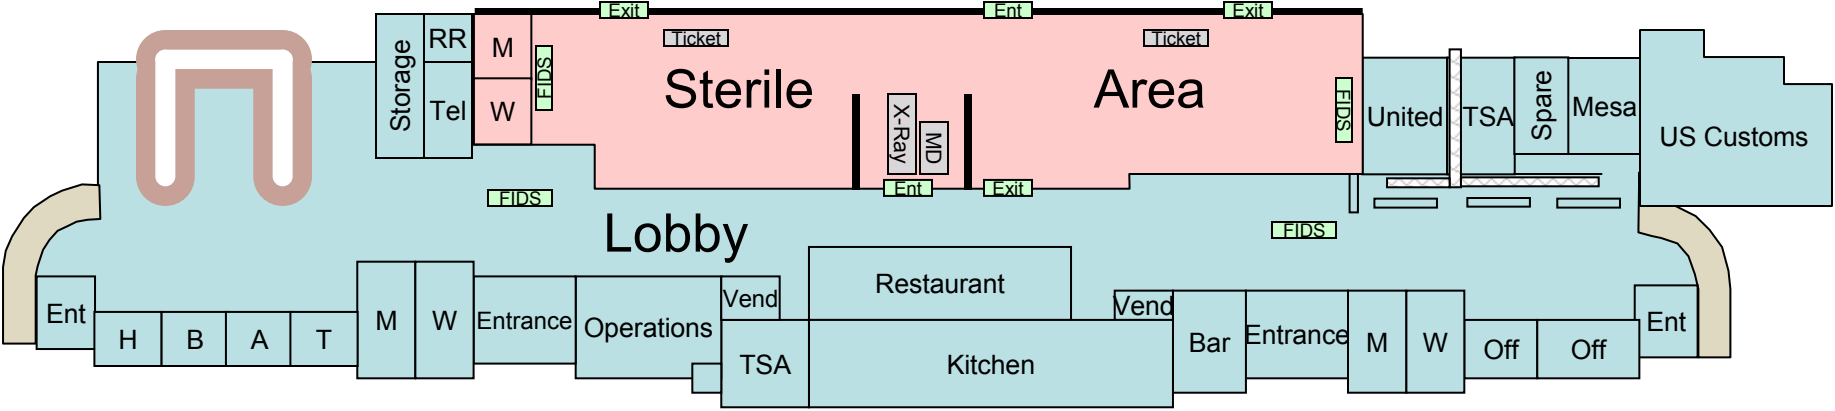

Final Result

